PROGRESS SCHEDULE - CONTRACT 04

Commencement date	:	16 December 2005	Time for completion	:	47 months	Planned total progress	:	83.5 %
Contract completion date	:	15 December 2008	Time elapsed	:	43 months	Actual total progress	:	76.4 %
Extended Completion date	:	31 October 2009	% Time elapsed	:	91%	Ahead (+) / Behind (-)	:	-7.1 %

Scheduled duration and percentage accomplishment : 45 100

Actual duration and percentage accomplished to date : 50

Scheduled progress :

Revised Scheduled progress :

Actual progress :

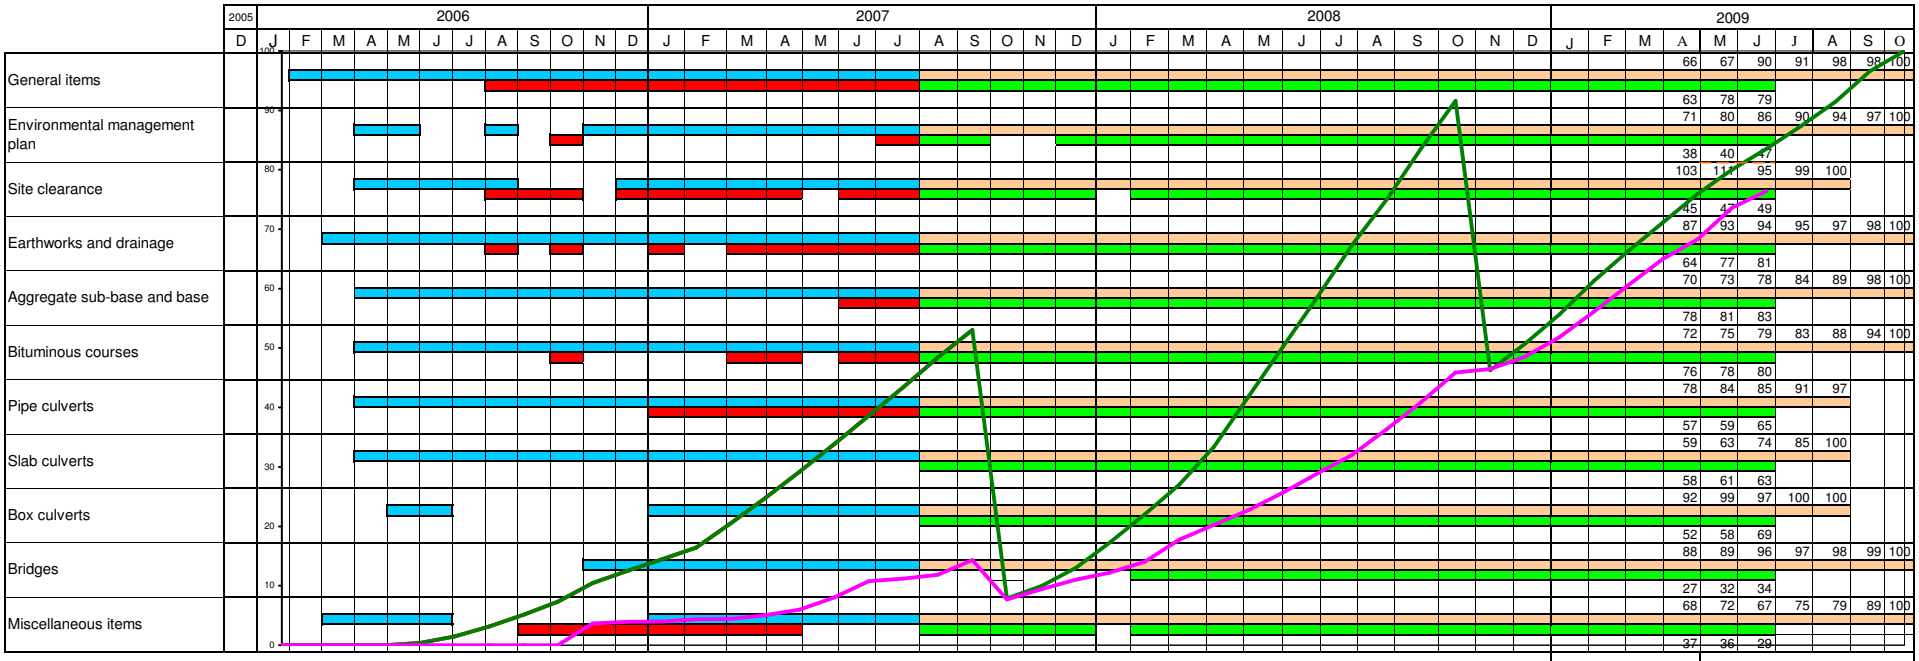

| | | | | | | | |
